







IPAO Milestone Schedule by MD

9-18-06

Task Name	MD			2006				2007				2008
		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
<u>Space Communications Program (Carraway, Larson) - PIR</u>	<u>SOMD</u>			1-3					 11-16			
SCAWG Report Complete	SOMD				 2-28							
ICA Complete	SOMD								10-4			
Brief SOMD	SOMD								11-9			
Brief APMC	SOMD								11-16			

Task



Milestone



Review Duration - Negotiated



Progress



Complete Milestone



Review Duration - Not Negotiated



IPAO Milestone Schedule by MD

9-18-06

Task Name	MD	2006						2007				2008	
		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
<u>OSTM Project (Smolka) - NAR (Complete)</u>	<u>SMD</u>	7											
<u>MSL Project (Calloway, Greathouse) - PNAR (Complete)</u>	<u>SMD</u>	10-3											
<u>JWST Project (Frazier, Fernandez) - SR</u>	<u>SMD</u>												
Receive Preliminary Cost/Schedule Data from Project	SMD												
Team Approved	SMD												
ToR Approval Process Complete	SMD												
Conduct Site Review (NGST)	SMD												
ICE Reconciliation with Program	SMD												
Brief PMC	SMD												
Issue the Report	SMD												
<u>New Frontiers Program (Thomas,Tecelote) - PIR</u>	<u>SMD</u>												
Team Approved	SMD												
ToR Approval Process Complete	SMD												
Conduct Site Review	SMD												
Brief Program/Project	SMD												
Brief APMC	SMD												
<u>STP Program (Chung, Fairbairn) - PIR</u>	<u>SMD</u>												
ToR Approval Process Complete	SMD												
Conduct Site Review & Team Caucus	SMD												
Brief SMC AA	SMD												
Brief APMC	SMD												
<u>MSL Project (Calloway, Greathouse) - NAR</u>	<u>SMD</u>												
Project PDR	SMD												
CADRe Due	SMD												
IRT Caucus	SMD												
ICE Complete	SMD												
Brief Project	SMD												
Brief APMC	SMD												

Task



Milestone



Review Duration - Negotiated



Progress



Complete Milestone




Review Duration - Not Negotiated







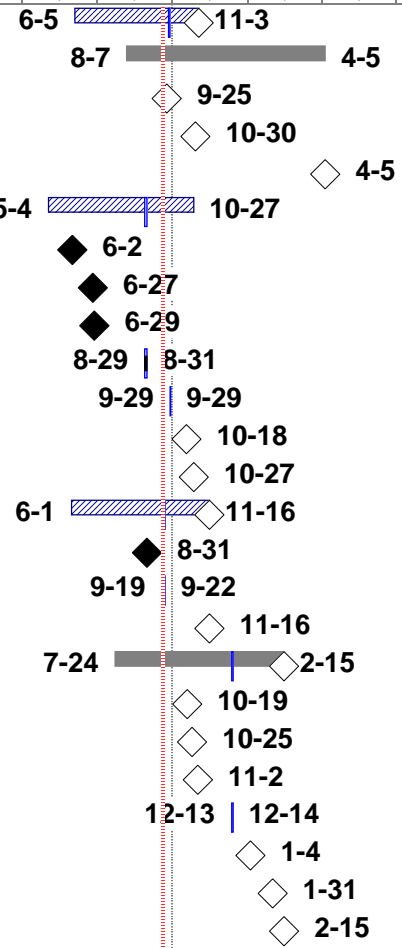

IPAO Milestone Schedule by MD

9-18-06


Task Name	MD	2006				2007				2008			
		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
<u>Mars Exploration Program (Calloway, Copeland) - PIR</u>	<u>SMD</u>					6-5							
<u>JWST Phase I - Technology (Frazier, Fernandez) - NAR</u>	<u>SMD</u>					8-7				4-5			
Team Approved	SMD												
ToR Approval Process	SMD												
Brief PMC	SMD												
<u>ST-8 Project (Cheek, Chromik) - NAR</u>	<u>SMD</u>					5-4							
Receive Preliminary CADRe from Project	SMD												
ToR Approval Process Complete	SMD												
Team Approved	SMD												
Conduct Site Review	SMD												
ICE Complete	SMD												
SMD Prebrief	SMD												
ST8 Confirmation Review	SMD												
<u>MMS Project (Chung, Fairbairn) - PNAR</u>	<u>SMD</u>					6-1							
ToR Approval Process Complete	SMD												
Conduct Site Review & Team Caucus	SMD												
Brief SMD AA	SMD												
<u>New Millennium Program (Cheek, Larson) - PIR</u>	<u>SMD</u>					7-24							
Team Approved	SMD												
ToR Approval Process Complete	SMD												
Receive ICA Data	SMD												
Conduct Site Review	SMD												
ICA Complete	SMD												
Brief Program/Project	SMD												
Brief APMC	SMD												



Task		Milestone		Review Duration - Negotiated	
Progress		Complete Milestone		Review Duration - Not Negotiated	

IPAO Milestone Schedule by MD

9-18-06

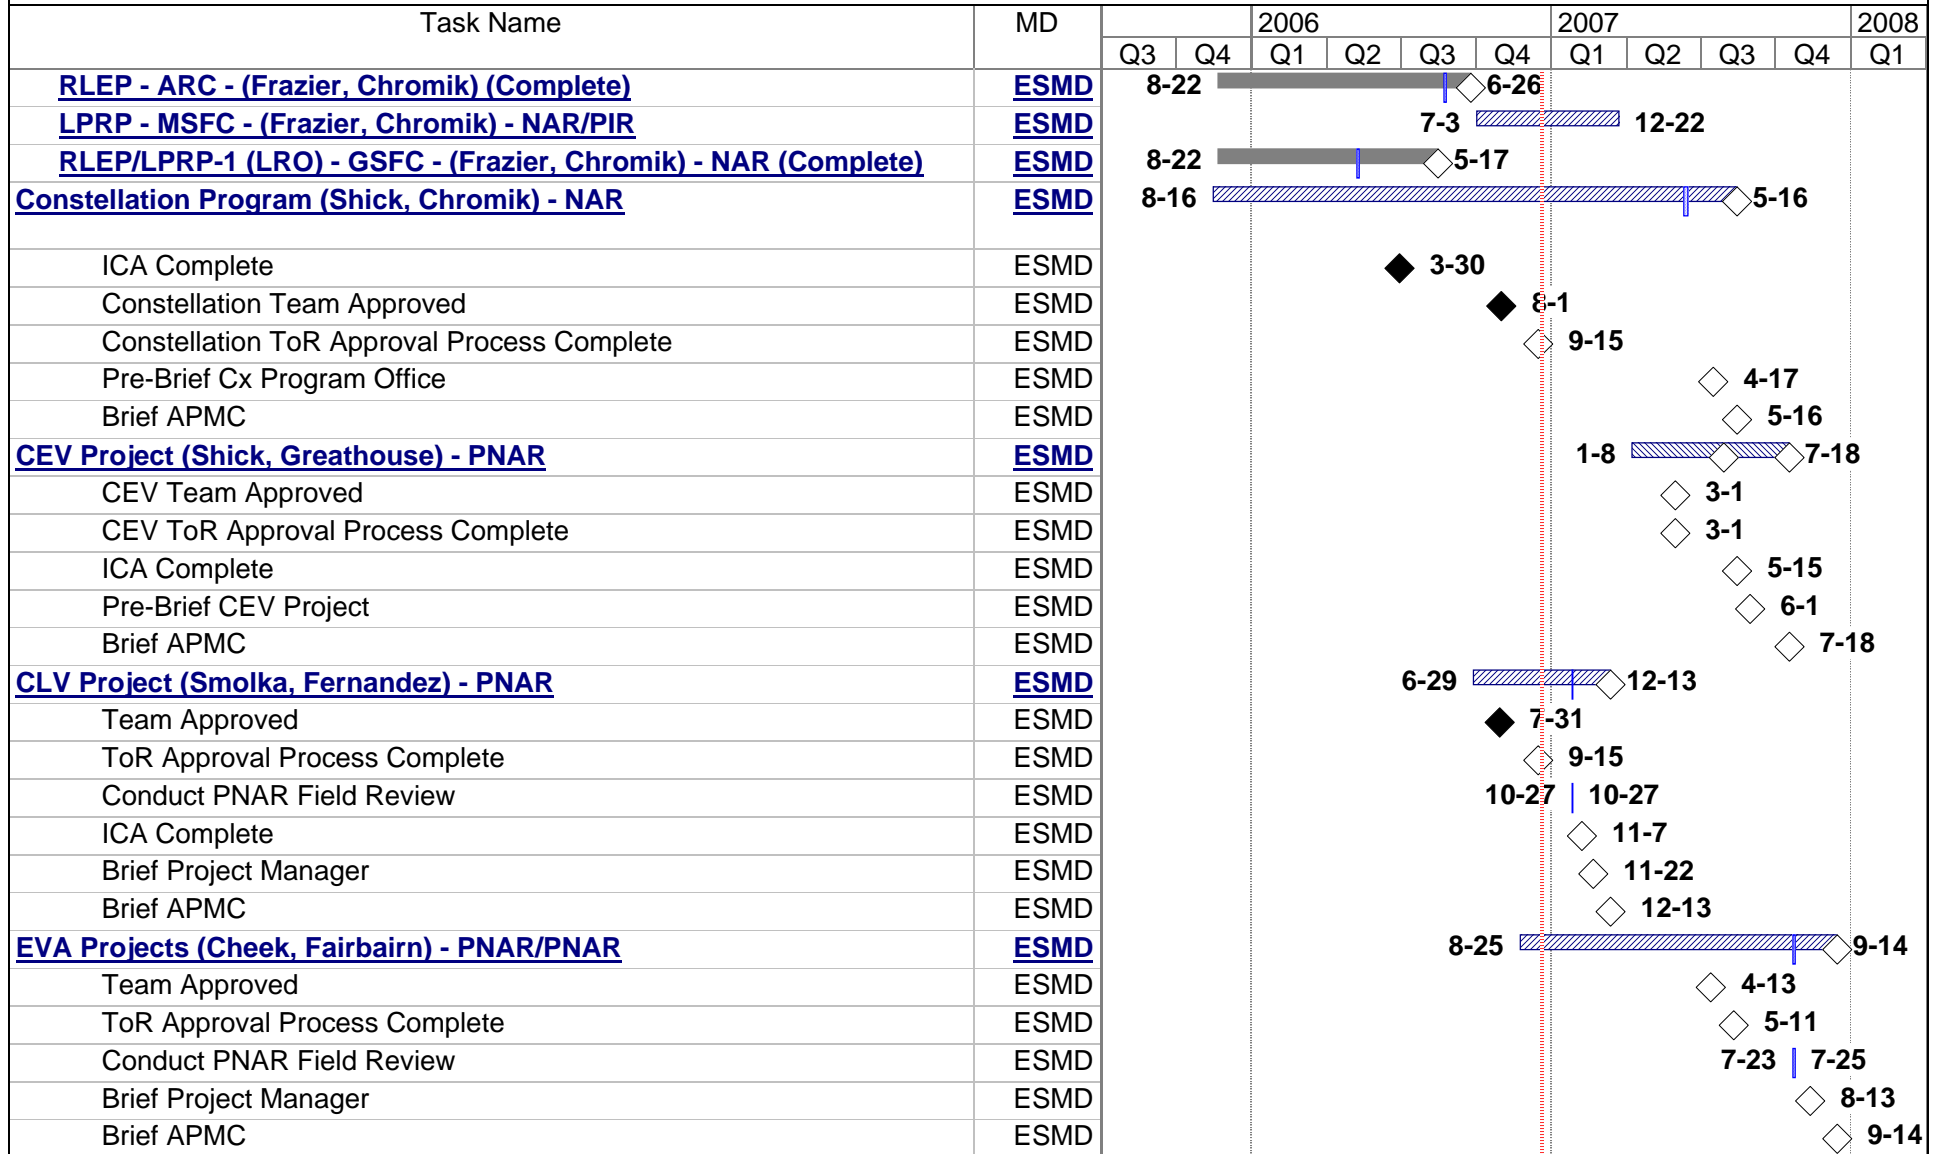

Task



Milestone



Review Duration - Negotiated



Progress



Complete Milestone



Review Duration - Not Negotiated



IPAO Milestone Schedule by MD

9-18-06

Task Name	MD			2006				2007				2008
		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
<u>Ground Operations Project (Shaw, Chromik) - PNAR</u>	<u>ESMD</u>						7-31	12-13				
Team Approved	ESMD							9-1				
ToR Approval Process Complete	ESMD							9-15				
Conduct PNAR Field Review	ESMD						10-27	10-27				
ICA Complete	ESMD							11-7				
Brief Program/Project Manager	ESMD							11-22				
Brief APMC	ESMD							12-13				
<u>Mission Operations Project (Carraway, Chromik) - PNAR</u>	<u>ESMD</u>							2-23				9-25
Team Approved	ESMD								3-29			
ToR Approval Process Complete	ESMD								4-13			
ICA Complete	ESMD								6-1			
Conduct PNAR Field Review	ESMD								6-25	6-29		
Brief Program/Project Manager	ESMD											9-5
Brief APMC	ESMD											9-2

Task



Milestone



Review Duration - Negotiated



Progress



Complete Milestone








Review Duration - Not Negotiated



IPAO Milestone Schedule by MD

9-18-06

Task Name	MD					2006				2007				2008
		Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1		
<u>IEM Program (Cheek, Larson) - PIR (Complete)</u>	<u>MSO</u>		9-30											
<u>Innovative Partnership Program (Canga) - SR</u>	<u>MSO</u>													
Team Approved	MSO													
Conduct Review Meeting I	MSO													
ToR Approval Process Complete	MSO													
Brief Program/Project	MSO													

Task		Milestone		Review Duration - Negotiated	
Progress		Complete Milestone		Review Duration - Not Negotiated	
